

PROGRESS BULLETIN

4RF- POST FLOOD REHABILITATION AND RECONSTRUCTION PROJECTS IN SINDH

MONTH OF AUGUST 2025

**RECOVERY & RECONSTRUCTION UNIT (RRU) SINDH
PROJECT COORDINATION & MONITORING UNIT (PCMU)
PLANNING & DEVELOPMENT DEPARTMENT
GOVERNMENT OF SINDH**


Background:

Recovery & Reconstruction Unit (RRU) Sindh has been established at PCMU - Directorate of Sindh Water & Barrages Improvement vide P&D Department's notification dated 28th March, 2024 for providing coordination support and implementation facility to all Project Directors of post floods 4RF Projects in Sindh.

Purpose/Tasks:

- ❑ Provide project preparation support and implementation facility to post flood project implementing departments / agencies.
- ❑ Boost up progress of ongoing post flood projects in Sindh through oversight committee headed by Chief Economist, P&D Department.
- ❑ Bridge between federal and provincial government setup of 4RF for providing coordination support and facilitate all Project Directors of post floods projects in Sindh in case any guidance is required in procurement and financial management matters.
- ❑ Serve as Secretariat of 4RF Provincial Steering Committee headed by Chairman P&D Board.

Structure

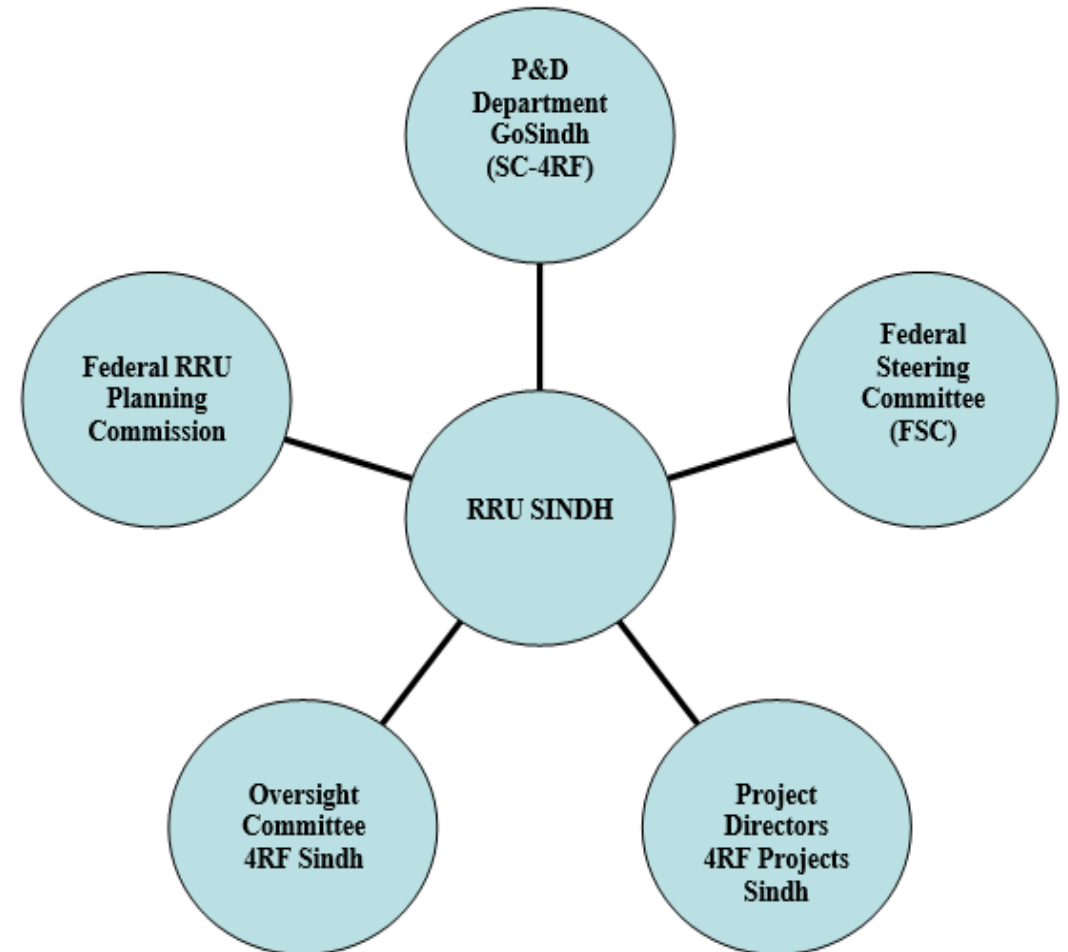

Institutional Setup in Sindh:

Provincial Steering Committee Notified on 3 rd May 2023		Oversight Committee Notified on 28 th March 2023 & Re-notified on 12 th Sept. 2024		
Chairman P&D Board, GoSindh	Chairman	Chief Economist, P&D Department, GoSindh	Convener	
Secretary to Government of Sindh 1. Finance Department 2. Local Government & Housing Town Planning Department 3. Agriculture Department 4. I&C, S&GA Department 5. Irrigation Department 6. Works & Services Department 7. Health Department 8. Livestock & Fisheries Department 9. School Education Department 10. Environment & Climate Change Department 11. Industries & Commerce Department 12. Public Health Engineering & RD Department 13. Culture & Tourism Department 14. Social Protection Department 15. Rehabilitation Department.	Member	Additional Secretary (Dev.) Finance Department, GoSindh	Member	
	Member	Member/Chiefs, P&D Department, concerning 4RF	Member	
	Member	Project Directors, All Post Flood Emergency Projects Sindh ❑ Housing Reconstruction Project ❑ FERC-SWAT ❑ Integrated Health & Population Program ❑ Social Protection Delivery System ❑ Rehabilitation of Irrigation System ❑ Livelihood, Rescue, Rehabilitation of Roads, WS & Drainage ❑ Rehabilitation & Reconstruction of Roads ❑ Rehabilitation of School/Education Facilities	Member	
	Member			
	Member			
	Member			
	Member			
	Member	Chief (Foreign Aid) P&D Department, GoSindh	Member	
	Member	Representatives of Administrative Departments of 4RF Projects of Sindh	Member	
	Member	Project Coordinator, PCMU-SWS&BI, P&D GoSindh	Secretary	
	Member	Purpose: Serve as Secretariat of 4RF Provincial Steering Committee. Facilitate all PDs of flood projects in case of guidance is required in procurement and financial management matters. Development and Implementation of (4RF) Monitoring and Evaluation (M&E) Results Framework, which could be integrated at Federal Level.		
	P&D Department, Government of Sindh 1. Special Secretary (Dev.) 2. Members P&D Board (Social Sector) 3. Members P&D Board (Services), 4. Members P&D Board, NR 5. Members P&D Board (E&T) 6. Chief Economist	Member	Recovery & Reconstruction Unit (RRU) Sindh notified on 28 th March 2023	
		Member	Directorate of Sindh Water & Barrages Improvement vide P&D Department, Government of Sindh for providing coordination support and implementation facility to all Project Directors of post floods 4RF Projects in Sindh.	
		Member		
		Member		
Member				
Purpose: Provide overall guidance, facilitate coordination, review progress of projects and resolve bottlenecks, oversee functions of Sindh RRU.				

Details of Damages (Houses, Crops & Infrastructure)




12.4 million people affected
5 million people pushed into **poverty**



3.8 million acres of crops damaged
4.3 million people facing food insecurity threat



1500 Health Facilities Damaged
20,000 Schools Damaged



436,435 livestock perished
2.15 million people facing job disruption/loss



2.1 million houses damaged



Sindh 4RF Projects Snapshot:

Total Sindh Portfolio: 11 Projects with approved cost of US\$ 3,752.49 Million

Foreign Funding: Allocation of US\$ 3,127.89 Million (83%)

Local (GOS) Funding: An amount of US\$ 446.00 Million (17%) in 07 Projects

World Bank (WB): 07 Projects with approved cost of US\$ 2,240.93 Million (60%)

Asian Development Bank (ADB): 4 Projects with approved cost of US\$ 886.96 Million (24%)

World Bank + Islamic Development Bank: 02 Projects with approved cost of US\$ 1,400 Million (37%)

Initial approved Portfolio: 09 Projects with approved cost of US\$ 2,584.42 Million

Additional Projects: 02 Projects with approved cost of US\$ 600 Million (SSPA-WB & Housing Ph-2-ADB)

Completed: 03 Projects (100%)

Total Cumulative Expenditure: US\$ 1,992.10 Million (53%)

Details of all project are provided in next slide

Project-Wise Financial & Physical Progress Status:												In Million US\$
Sr.No.	Projects	Sector	Dev. Partner	Total Cost	Donor Funds	ADP/ PSDP	Approving Authority	Project Approval Date	Project Duration (Starting Year – Completing Year)	Physical Progress %	Cumulative Spending	Financial Progress
					Allocation	Share						
On-going Projects												
1	Flood Response Emergency Housing Project (Revised)	Housing, Infra	WB, IsDB	1,597	1,150	447	ECNEC	04.01.2023 (Original)	Jan. 2023 – Dec. 2026	74%	975.00	61%
2	Sindh Flood Emergency Rehabilitation Project (Irrigation Component220.066 m)	Irrigation, Water	W.B	538.066	220.066	0	ECNEC	06.12.2022	Jan. 2023 -Dec. 2027	99%	217.651	99%
	Sindh Flood Emergency Rehabilitation Project (P&D Component \$318 m)	Transport & Communication, Municipal Serv.			288	30	ECNEC	06.12.2022	Jan. 2023 - Dec.2027	97%	299.00	94%
3	Sindh Water & Agriculture Transformation (SWAT) Project	Water	IDA + WB	98	98	0	ECNEC	06.12.2022	Dec. 2022 - Dec. 2028	72%	69.65	71%
4	Sindh Integrated Health and Population Program	Health	IsDB + WB	280	250	30	ECNEC	04.01.2023	Jan. 2023 - Dec.2027	17%	11.42	4%
5	Sindh School Rehabilitation Project Under Flood Restoration Program (ADB Emergency Assistance)	Education	ADB	302.5	275	27.5	ECNEC	11.12.2023	Jan.2024 - June 2028	7%	23.51	8%
6	Flood Response Emergency Housing Project (Phase-II) ADB/GOS Financing	Housing, Infra	ADB	440	400	40	ECNEC	28-10-2024	2024 - 2027	59%	233.66	53%
Cross - Provincial Project												
7	Emergency Flood Assistance Project (EFAP) — on Farm Water Management	Infra	ADB	220	199.9	20.1	ECNEC	12/15/2022	Jan. 2023 – Dec. 2027	73%	95.29	43%
8	DRR Project for Rehabilitation / Reconstruction	DRR	ADB / NDRMF	12.06	12.06	0	MoPDSI	Ph.1) 26.04.2023 Ph.2) 22.09.2023		100%	12.06	100%
Completed Projects												
9	Sindh Irrigated Agriculture Productivity Enhancement Project (2015)	Agriculture	W.B	7.86	7.86	0	PDWP	01.09.2022		100%	7.86	100%
10	Competitive & Livable City of Karachi (2019 - Repurposed)	Governance	W.B	27	27	0	GoS	08.09.2022		100%	27.00	100%
Other Project												
11	Strengthening Social Protection Delivery System in Sindh – SSPDSS	Health	WB	230	200	30	ECNEC	06.01.2023	Jan. 2023 – Dec. 2027	78%	20.00	9%
Grand Total				3,752.49	3,127.89	624.60				62%	1,992.10	53%

Progress/Achievements of Current Month (August-2025):

- ❑ A 4RF Projects review meeting was held on August 13, 2025, organized by Ministry of Planning, Development, and Special Initiatives (M/o PD&SI) under the Chairmanship of Director General of the Federal Resilient Recovery Unit (RRU), M/o PD&SI. The officials of P&D Department, RRU Sindh and the team of all 4RF projects in Sindh participated the meeting virtually.
- ❑ A Coordination and Consultation Session on the 2025 Flood Damage and Needs Assessment was held on September 01, 2025 under the Chairmanship of Member I&RC, MoPDSI. The Officials of the P&D Department, RRU Sindh, and teams from all 4RF projects in Sindh joined the meeting virtually..

Progress/Achievements of Current Month (July-2025):

- ❑ The Fifth meeting of the Oversight Committee of 4RF was held on 17th July 2025 in the Committee room of P&D Department, Karachi. The meeting chaired by Mr. Mohammad Aslam Soomro, Chief Economist / Convenor of the Committee, P&D Department, Government of Sindh.
- The Committee reviewed implementation progress (Financial and Physical) of projects that come under the umbrella of 4RF/ RRU Sindh.
- The committee also discussed the Implementation and Reporting Mechanism of M&E Framework for each Project, followed by the development of Province-based framework required by the Federal RRU.
- Minutes of Meeting prepared and submitted for approval of Chairman.

- ❑ The Provincial RRU Sindh facilitated the team of federal RRU for arranging the capacity building workshop on Project Planning and Management held on July 23, 2025, at Karachi. Mr. Nazeer Ahmed Memon, Project Coordinator, PCMU / RRU Sindh, participated as the chief guest of the event.

- ❑ Followed by a workshop, a meeting of the Provincial RRU Sindh Working Group was held on July 24, 2025, in the Committee room of the PCMU, P&D Department, Government of Sindh, Karachi. Chief Economist chaired the meeting and participated by the Federal RRU team, UNDP, Project Directors, along with M&E Specialists, and presented and discussed the project-specific M&E Framework.



Progress/Achievements of the Month of June-2025:

- ❑ The second meeting of Provincial Steering Committee (PSC) of 4RF was held on 25th June, 2025 under the Chairmanship of Chairman P&D Board.
- The Committee reviewed project progress with project based Result M&E Framework and directed Project Director, ADB financed Roads Infrastructure project for preparation and submission of its Project RBM within a week time.
- Further directed that all PDs will submit the RBM implementation progress on the prescribed format to federal RRU on regular basis.
- A team of M&E Specialists of projects was formed for development and submission of Provincial based RBM as required by Federal RRU.



- ❑ In compliance of the decision of PSC, follow-up meeting with the officials of 4RF– ADB Financing Rehabilitation of Roads Infrastructure Project was arranged at PCMU on June 27, 2025 chaired by PC- PCMU, discussed way forward and methodology for preparation of M&E Framework of Project.



- ❑ The overall 4RF Provincial Progress Summary of all 4RF Projects for the month of June, 2025 collected and consolidated on the prescribed format and shared with Federal RRU through P&D Department for placement on Dashboard maintained by Federal RRU.

Progress/Achievements of Month of May-2025:

- ☐ In response to the request from the Federal RRU, revised Results-Based Monitoring (RBM) reports for all 4RF projects in Sindh were collected, consolidated, and submitted to the Federal RRU on May 13, 2025.
- ☐ Coordinated and participated in the National Consultative Workshop on the 4RF along with all nominated M&E officers from 4RF Project offices, organized by the Ministry of Planning, Development & Special Initiatives (M/o PD&SI) on May 14, 2025, in Islamabad.
- ☐ The Workshop was chaired by the Director General of Federal RRU and aimed to engage all the stakeholders to finalize and consolidate the 4RF Results Framework, ensure its alignment with national priorities, and enhance M&E mechanisms for post-flood recovery and reconstruction.
- ☐ During the workshop, 4RF SRO-based Provincial Results Framework was developed, consolidated and shared with the Federal RUU, under the guidance of the Consultant (RBM Framework), Federal RRU.
- ☐ In accordance with the decisions made during the workshop held on 14th May, 2025, revised Results-Based Monitoring (RBM) reports for all 4RF projects in Sindh were collected, consolidated, and submitted to the Federal RRU on May 26 & May30, 2025.
- ☐ The overall 4RF Provincial Progress Summary of all 4RF Projects for the month of May, 2025 collected and consolidated on the prescribed format and shared with Federal RRU through P&D Department for placement on Dashboard maintained by Federal RRU.
